

# Flood Diversion Authority April 2016 Report

Presented by

Program Management Consultant

# March Activities

- ▶ ND Water Topics (Mar 7-8)
- ▶ ND SWC Dam Permit coordination and follow-up
- ▶ Continued support/coordination of MN EIS and Dam Safety Permit
  - *MN DNR presentation Mar 1 (Moorhead)*
  - *Executive Sponsor meeting Mar 29*
- ▶ Released Updated Program Cost Estimate (\$2.1B)
- ▶ Lawsuit Ruling – dismissed all federal claims

# March Activities

## 💧 Conducted/Participated in Design reviews:


- *WP-26 (Diversion Inlet) – USACE BCOE review and meeting (Mar 17)*
- *WP-42F.2 (2<sup>nd</sup> St. So. Flood Control) – 95% review*
- *WP-42G (Landscaping and Plantings) – 35% review*

## 💧 Administered Construction Bid

- *WP-42F.1N (2<sup>nd</sup> St. N, North of Pump Station Flood Control)*

# April/May Priority Areas

- Financial Plan Development
- JPA Approval
- PPA Development
- P3 Advancement

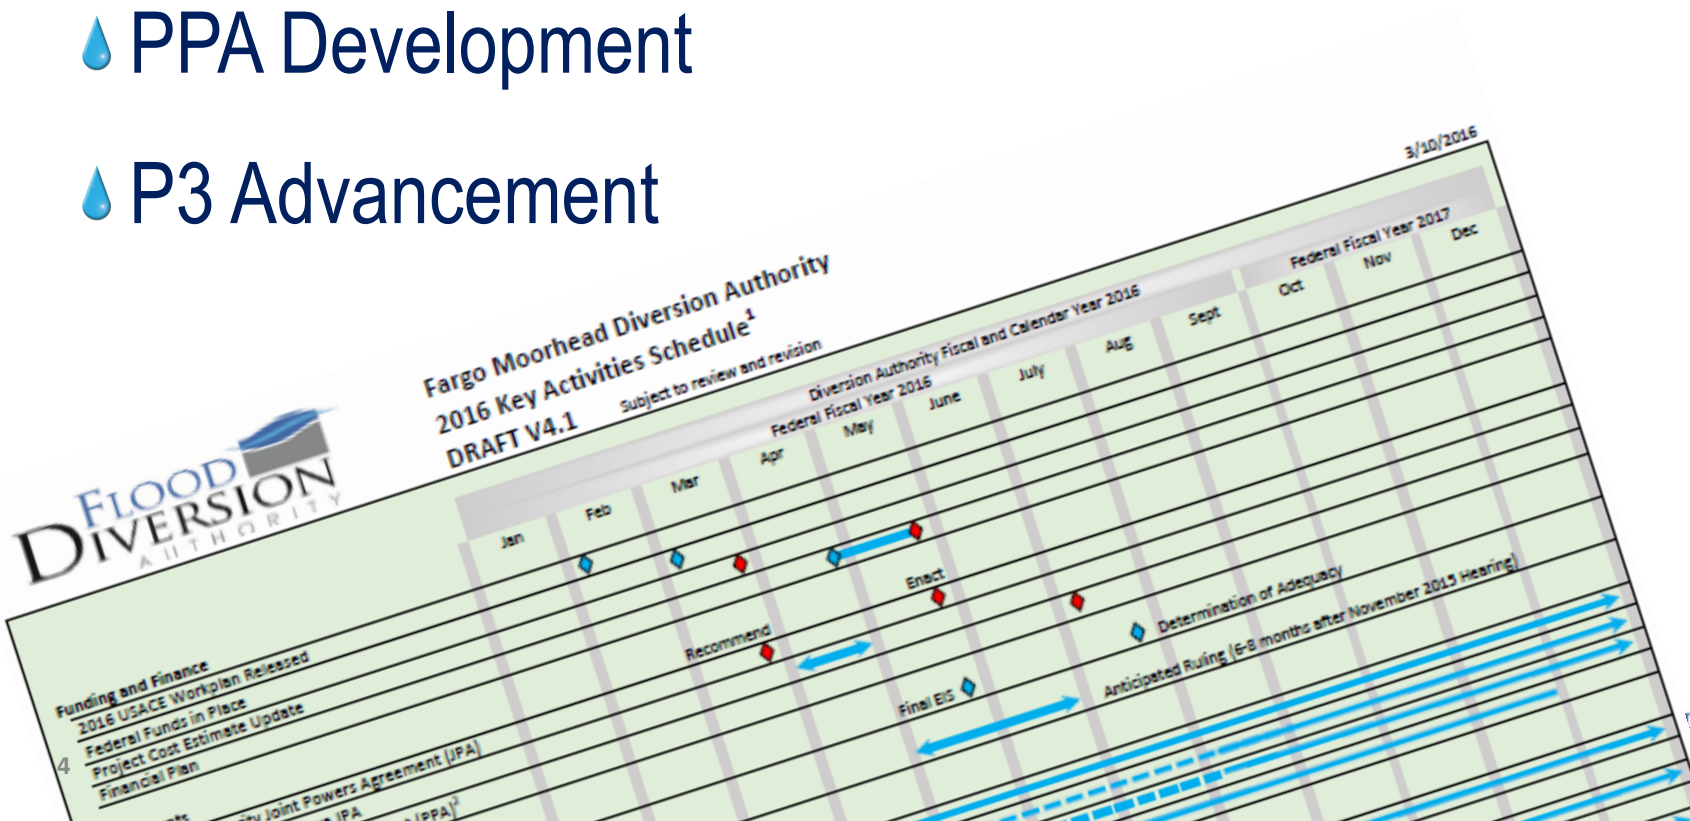

# In Town Levees

## WP-42A.1/A.3 (4th St N Pump Station) – April 2016

- 💧 Pump station complete pending wet test of pumps
- 💧 Addressing box culvert concerns before testing can go forward
- 💧 After pump station goes operational, construction to continue rest of year (generator and building, demo old pump station)



# In Town Levees

## WP-42A.2 (2<sup>nd</sup> Street Pump Station) – April 2016

- 💧 Pump station approaching 100% completion
- 💧 Awaiting permanent power (other project) before starting pump tests
- 💧 Estimate operational by August 15



# In Town Levees

## WP-42F.1S (2<sup>nd</sup> St Flood Control, South) – April 2016

- Resumed work at end of March after winter break
- Removed former 2<sup>nd</sup> Street roadway
- Excavating for flood wall
- Coordinating schedule revisions with Contractor to accommodate other City of Fargo projects



# WP-42C.1 (Howard Johnsons Demolition)


## WP-42C.2 (Park East Demolition) – April 2016

### WP-42C.1 (Demo HoJo, etc.)

- 💧 Completed demo of old Shakey's Pizza
- 💧 Wall construction in Fargo Public Schools warehouse underway
- 💧 Discovered additional asbestos in Howard Johnson, will extend timeline ~30 days

### WP-42C.2 (Demo Park East)

- 💧 Site activity to resume week of April 25 to remove final components
- 💧 Complete by May 15

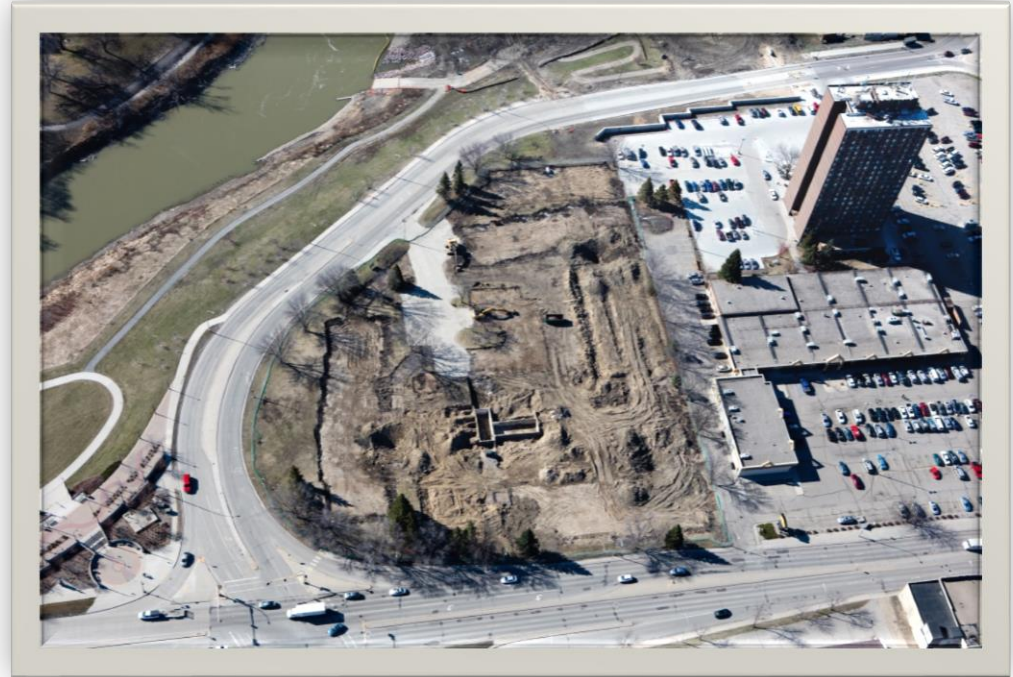



# WP-42H.2 (El Zagal Phase 2) – April 2016

- Completed asbestos abatement in homes
- Home demo underway
- Levee construction to begin next month



# WP-42I.1 (Mickelson Levee Extension) – April 2016

- Field work to begin week of April 25 (asbestos abatement and home demo)
- Levee construction to begin in June

# Planned Bid Schedule – In Town Levees

- 💧 WP-42F.1N (Flood Control 2nd St N) – April 2016
  - *Opened bids April 7*
  - *Recommendation to award today; project start next month*
- 💧 WP-42F.2 (Flood Control 2nd St. South) – May 2016
  - *Levee, roadway closure*

# Next

- 💧 Corps Report
- 💧 Budget Presentation
