

# Flood Diversion Authority March 2016 Report

Presented by

Program Management Consultant


# February Activities

- 💧 Ongoing Construction Support
- 💧 Responded to comments on MN EIS
- 💧 USACE 404 Permit Application Support
- 💧 Submitted MN and ND Dam Safety/Construction Permits
- 💧 Reported to Legislature at ND Water Topics Overview Committee

# March/April Priority Areas

## 💧 2016 Activity Schedule

- *Cost Estimate and Financial Plan Presentations*
- *JPA Approval Process*
- *Respond to USACE PPA comments from USACE HQ*
- *Due Diligence and Preparation of RFQ and RFP*

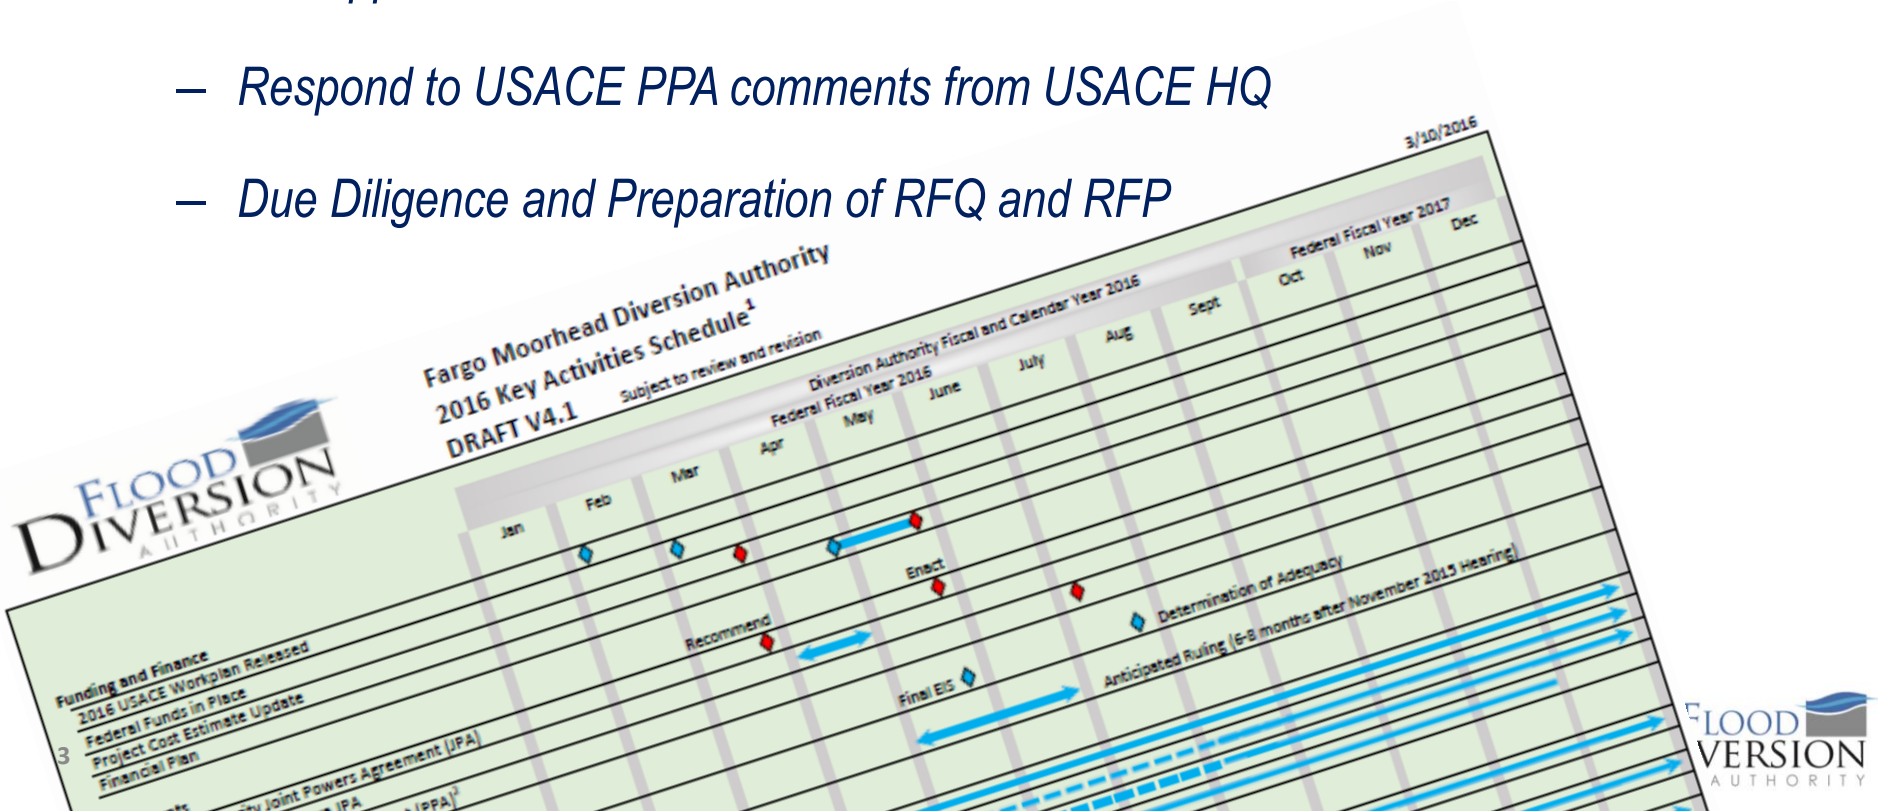

# In Town Levees

## WP-42A.1/A.3 (4th St N Pump Station) – March 2016

- 💧 Pump station structure and electrical complete; preparing for pump tests
- 💧 Addressing construction concerns with box culvert slope





# In Town Levees

## WP-42A.2 (2<sup>nd</sup> Street Pump Station) – February 2016

- Contractor completed Milestone 1A (pump station structure, finishes, electrical, and pump install)
- Work activity to drop off until permanent power install (under different contract) this summer



# **WP-42C.1 (Howard Johnsons Demolition)**

## **WP-42C.2 (Park East Demolition)**

### **WP-42C.1 (Howard Johnsons Demolition)**

- 💧 Mobilized to site, installed fencing
- 💧 Beginning preparations for abatement work

### **WP-42C.2 (Park East Demolition)**

- 💧 Completed demolition and clean-up of the building with exception of one basement
- 💧 Basement contains previously unknown asbestos, will require new Change Order to address

# WP-42H.2 (El Zagal Phase 2) – March 2016

- 💧 Project awarded, beginning pre-construction coordination and admin
- 💧 On-site work scheduled to begin end of March



# Planned Bid Schedule – In Town Levees

💧 WP-42F.1N (Flood Control 2nd St N) – Mar 2016

– *Floodwall, road relocation*

💧 WP-42F.2 (Flood Control 2nd St. South) – May 2016

– *Levee, roadway closure*



# Next

💧 Corps of Engineers report
