

# Public Outreach Report

Website, social media and media tracking analytics

Medium	June Analytics	Notes
www.FMDiversion.com	2,222 unique visitors Average for one month 10,005 page views, 3:54 min. Avg time on site.	Longer time on site this month
Twitter @FMDiversion	31 tweets 9 mentions 15.4K tweet impressions 6 new followers (great!)	Good engagement on construction pictures
Youtube.com/FMDiversion	1,533 views compared to 1,611 in March. Watch time was up 28 seconds	Most popular – Flyover and assessment mtg
Newsletter	1 newsletters sent 1,298 subscribers 42% open rate (good)	Industry average open rate is 22%

## Inlet Site Construction Update



- Legend**
- 1 – Future Channel Inlet
  - 2 – Southern preload
  - 3 – Northern preload
  - 4 – Left embankment
  - 5 – Right embankment



# Monthly Progress Report

July 27, 2017

## Major Activities in Past Month

- Preconstruction meeting held for Oxbow levee construction contract, continued with Oxbow home removals
- Preconstruction meeting held for CR 16 & 17 realignment contract
- Continued refining P3 RFP documents for a 28 July release to proposers
- Presented to the ND Water Topics Overview Committee
- Continued Phase 1 and Phase 2 land acquisitions
- Attended the federal court hearing, awaiting decision
- Assisted with Executive Director candidates' briefings and project tour

## Upcoming Priorities

- Send CLOMR notification letters to individual property owners upon approval by FEMA
- Respond to comments on the updated P3 RFP draft
- Continue land acquisition activities; initiate a flowage easement valuation study
- Develop crisis communications plans, policies and protocols
- Determine impacts, if any, of the court's ruling on the request for a preliminary injunction

# Financials



## Comprehensive Project


Program Budget	\$2,205,566,043
Expenditures To Date	\$368,344,264




## FY 2017

Program Budget	\$241,311,231
Expenditures To Date	\$35,943,378

## Construction

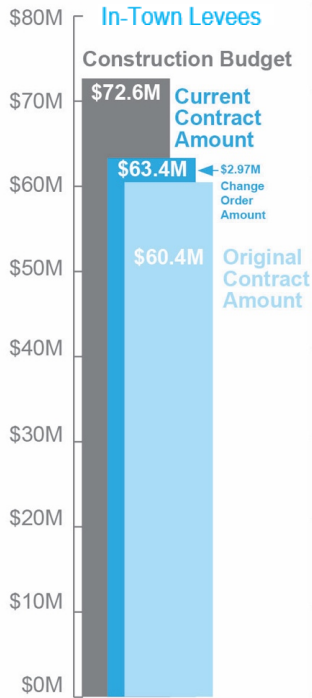

## Program Summary

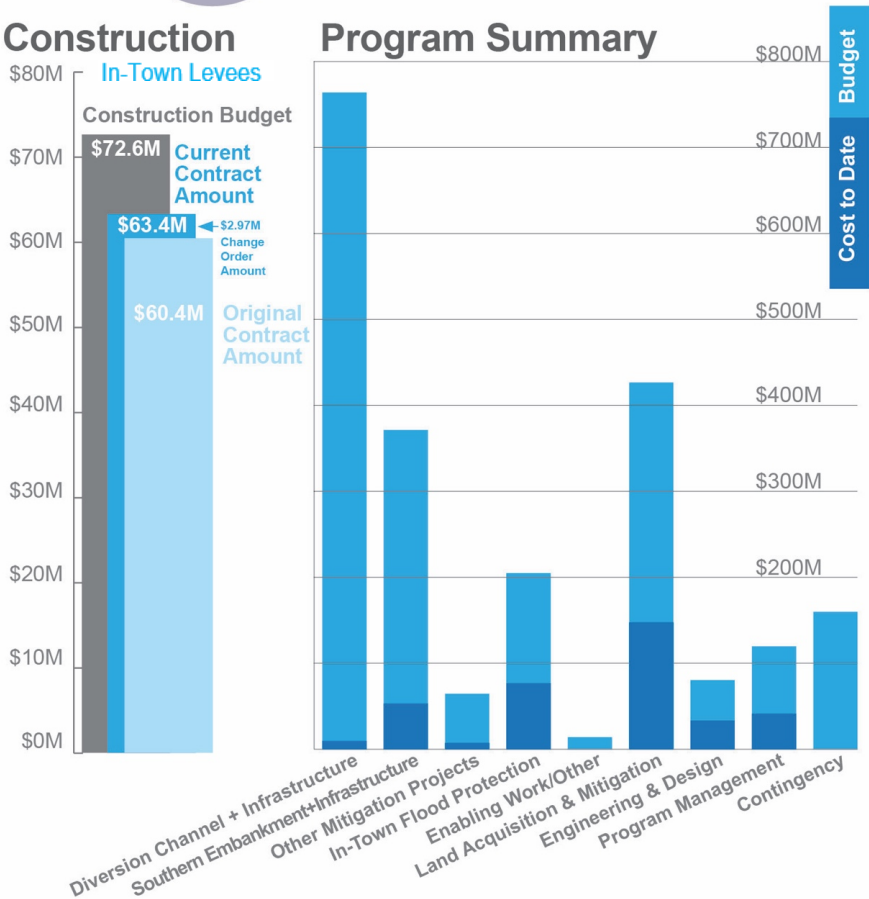

# Land



1,201 impacted parcels



Includes Channel, Mitigation Area, In-Town Levees and Bio/Geo Survey Parcels

## Work Packages

43E.3 – Oxbow City Park Relocation	Preparing revised design and bid documents for August award
43CD – Levee Construction and other work	Awarded to Meyer Contracting @ 7/13 DA Board Meeting
28A – County Road 16/17 Realignment	Awarded to Riley Brothers @7/13 DA Board Meeting

## Construction In-Town Levees

Marks where progress was reported last month

4th St. N Pump Station	99%
2nd St Pump Sta. Gatewell	99%
HoJo, Old Shakey's, FPS Demolition	100%
Park East Demolition	100%
Flood Control, 2nd St N, S of PS	97%
Flood Control, 2nd St N, N of PS	100%
Dwtn Levees 2nd St South	100%
Dwtn Levees Landscaping	0%
El Zagal Area Flood Risk Mgt	100%
Mickelson Levee Extension	100%
