



# FARGO MOORHEAD DIVERSION PROJECT

# MONTHLY UPDATE

20 Sep 2023

## 1 Diversion Inlet Structure (DIS) – Construction

Structure includes 3-50 ft. wide Tainter gates. Construction is 97% complete. Construction completion date is currently estimated to be in November 2023 due issues related to the gate machinery.

Schedule for remaining primary features:

2023: Complete operating machinery install, seeding.

2024: Turf established.

## 2 Wild Rice River Structure (WRRS) – Construction

Structure includes 2-40 ft. wide Tainter gates. Construction is 91% complete and remains on schedule. The construction completion date is 3 December 2023. Constructing eastern earthen dam and bridge deck. Remaining schedule:

2023: Bridge deck, dam embankment, seeding.

2024: Turf established.

## 3 I-29 Raise – Construction

Includes approximately 4 miles of interstate raise between County Roads 16 and 18. Construction is 84% complete. Borrow ditch bridges are complete. Traffic to be switched to all new lanes by 1 November. Current construction completion date is 1 January 2024.

## 4 Southern Embankment – Reach SE-1 (Western Tieback) - Construction

Construction was completed 10 November 2022. Partial turnover to the Diversion Authority for Operations and Maintenance occurred on 29 December 2022. O&M Manual was provided for review 9 August 2023.

## 5 Red River Structure (RRS) - Construction

Structure includes 3-50 ft. wide Tainter gates. Construction is 30% complete. Construction completion date is 19 March 2026. Concrete placements for approach wall foundations and abutments ongoing. Completion date is 19 March 2026.

## 6 Drain 27 Wetland Mitigation Project Plantings - Construction

Native plantings 5-year contract awarded 17 May 2023. Completion date is 1 December 2027.

## 7 Drayton Dam Mitigation Project Design - Construction

Construction is 85% complete. Placement of the rock-arch rapids is complete. Riprap placement ongoing. Construction completion is 30 September 2023.

## 8 Southern Embankment – Reach SE-2A - Construction

Construction is 67% complete. Inspection trench and embankment foundations complete. Embankment construction ongoing. Scheduled completion date is 30 September 2024.

## 9 Southern Embankment Design – All remaining reaches are being designed.

SE-1B: BCOES review Sep 2023 ..... Contract award: February 2024


SE-2B: BCOES review complete 9 June 2023..... Contract award: April 2024

SE-3: 95% review starts Jan 2024..... Contract award: January 2025

SE-4: 65% review Sep 2023 ..... Contract award: May 2024

SE-5: 95% review starts Dec 2023..... Contract award: January 2025

OHB Reach 43B: BCOES review starts Oct 2023..... Contract award: February 2024

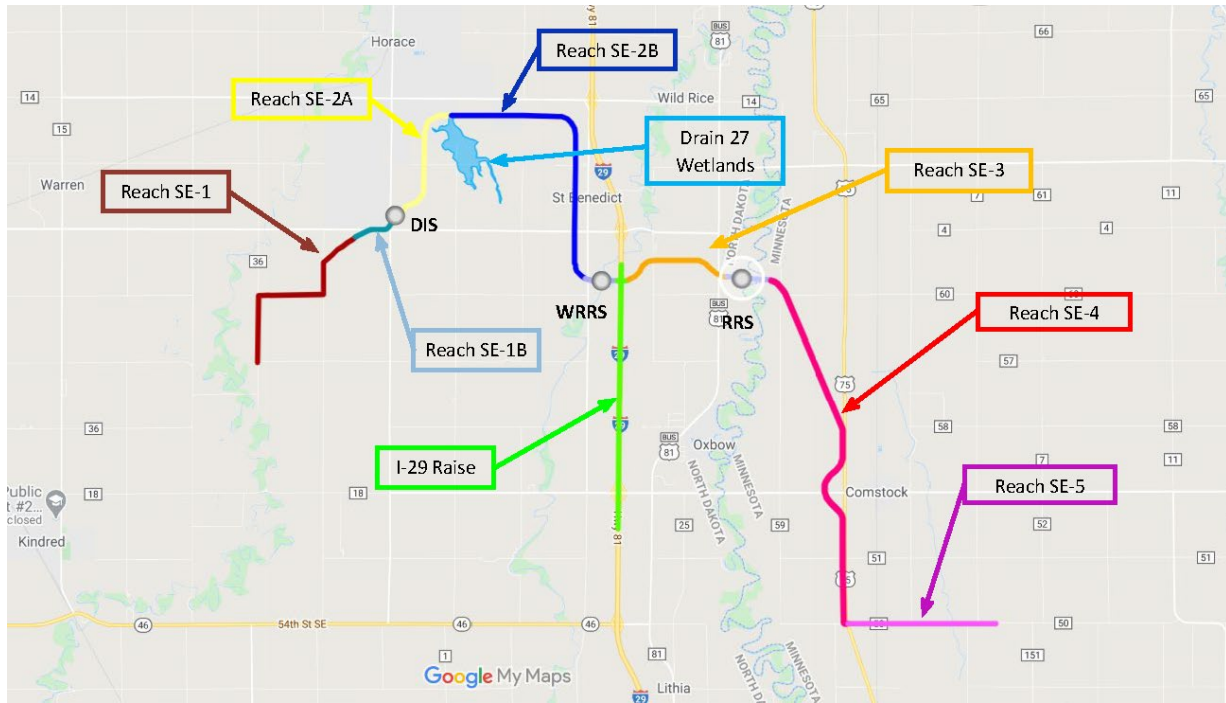

***Fargo-Moorhead Metro FRM – Federal Work/Southern Embankment and Control Structures***

DIS = Diversion Inlet Control Structure

WRRS = Wild Rice River Control Structure

RRS = Red River Control Structure
