



FARGO MOORHEAD DIVERSION PROJECT

MONTHLY UPDATE

19 Mar 2025

1 Diversion Inlet Structure (DIS) – Construction

Structure includes 3-50 ft. wide Tainter gates. Construction is 99% complete. Construction completion date will be revised pending outcome of modifications to the gate machinery design. Schedule for remaining work: 2025: Complete operating machinery corrections; commissioning and training.

2 Wild Rice River Structure (WRRS) – Construction

Structure includes 2-40 ft. wide Tainter gates. Construction is 98% complete. Revised construction completion date is 6 August 2025. Schedule for remaining work: 2025: Complete operating machinery corrections; commissioning and training.

3 I-29 Raise – Construction

Includes approximately 4 miles of interstate raise between County Roads 16 and 18. Construction is 100% complete. Partial turnover to MFDA occurred on 20 December and preparation of O&M documents is ongoing.

4 Red River Structure (RRS) - Construction

Structure includes 3-50 ft. wide Tainter gates. Construction is 74% complete. Construction completion date is 29 April 2026. Tainter gate #3 welding and concrete placements for approach apron and dam walls continues.

5 Drain 27 Wetland Mitigation Project Plantings - Construction

Native plantings 5-year contract awarded 17 May 2023. Completion date for wetland establishment is 1 December 2027.

6 Drayton Dam Mitigation Project Design - Construction

Construction is complete. Turnover to MFDA for O&M occurred on 28 Nov 2023. OMRRR manual will be finalized once MFDA provides comments.

7 Southern Embankment – Reach SE-2A - Construction

Construction is 76% complete but continues to be behind schedule. Scheduled completion date of 13 October 2024 was not met. Revised schedule and completion date pending.

8 FY2024 Contract Awards:

OHB Ring Levee: Awarded 22 February and is 50% complete. Contract completion date is 24 September 2025.

Reach SE-1B: Awarded 27 February and is 31% complete. Contract completion date is 13 March 2026.

Reach SE-2B: Awarded 11 March and is 37% complete. Contract completion date is 23 August 2026.

Forest Mitigation #1: Contractor is preparing lands for additional planting next season.


Reach SE-4: Awarded 28 May and is 5% complete. Contract completion date is 3 June 2026.

9 FY25 Contract Awards:

SE-3: Awarded 2 January 2025. Contract completion date is 11 September 2026.

SE-5: Contract was awarded on 30 January 2025 to BCSS, LLC of Tempe, AZ for \$10,097,097.

Forest Mitigation #2: Contract awarded 24 February 2025 to DJM Ecological Services for \$1.23M.

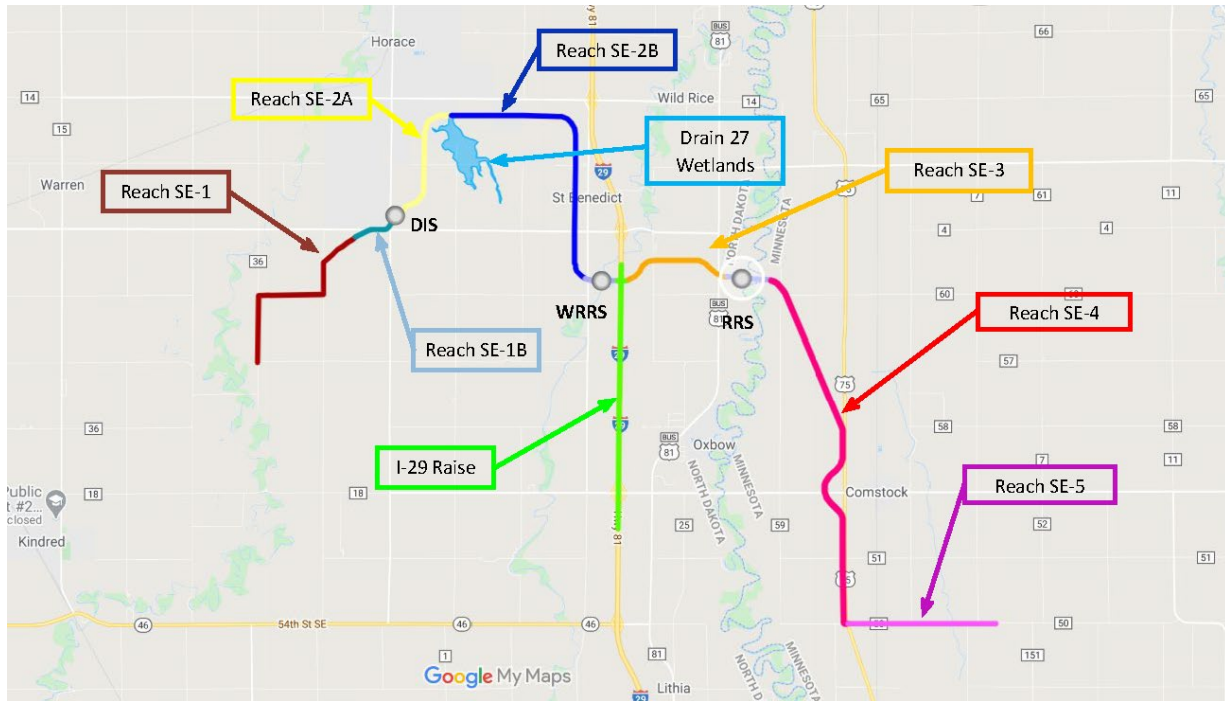

Fargo-Moorhead Metro FRM – Federal Work/Southern Embankment and Control Structures

DIS = Diversion Inlet Control Structure

WRRS = Wild Rice River Control Structure

RRS = Red River Control Structure
