



# FARGO MOORHEAD DIVERSION PROJECT

# MONTHLY UPDATE

16 April 2025

## 1 Diversion Inlet Structure (DIS) – Construction

Structure includes 3-50 ft. wide Tainter gates. Construction is 99% complete. Construction completion date is currently 30 June 25. Schedule for remaining work: 2025: Complete operating machinery corrections; commissioning and training.

## 2 Wild Rice River Structure (WRRS) – Construction

Structure includes 2-40 ft. wide Tainter gates. Construction is 98% complete. Revised construction completion date is 6 August 2025. Schedule for remaining work: 2025: Complete operating machinery corrections; commissioning and training.

## 3 Red River Structure (RRS) - Construction

Structure includes 3-50 ft. wide Tainter gates. Construction is 74% complete. Construction completion date is 29 April 2026. Tainter gate #3 welding, bridge assembly, and concrete placements for approach apron and dam walls continues.

## 4 Southern Embankment – Reach SE-2A - Construction

Construction is 76% complete but continues to be behind schedule. Scheduled completion date of 13 October 2024 was not met. Revised schedule and completion date pending.

## 5 Drain 27 Wetland Mitigation Project Plantings - Construction

Native plantings 5-year contract for wetland establishment. Completion date is 1 December 2027. Contractor replanting areas disturbed by adjacent producers.

## 6 FY2024 Contract Awards - Construction:

OHB Ring Levee: 50% complete. Contract completion date is 24 September 2025.

Reach SE-1B: 31% complete. Contract completion date is 13 March 2026.

Reach SE-2B: 45% complete. Contract completion date is 23 August 2026.

Forest Mitigation #1: Contractor to remobilize late April. Contract completion date is 31 Dec 2028.

Reach SE-4: 5% complete. Contract completion date is 3 June 2026.

## 7 FY2025 Contract Awards - Construction:

SE-3: Contractor anticipates mobilizing late April. Contract completion date is 11 September 2026.

SE-5: Contractor anticipates mobilizing early May. Contract completion date is 8 August 2026.


Forest Mitigation #2: Contractor to mobilize late April. Contract completion date is 31 Dec 2029.

## 8 I-29 Raise – Operations and Maintenance (OMRRR)

Turnover to MFDA occurred on 20 December and preparation of O&M documents is ongoing.

## 9 Drayton Dam Mitigation Project Design - Operations and Maintenance (OMRRR)

Turnover to MFDA for O&M occurred on 28 Nov 2023. OMRRR manual coordination continues.

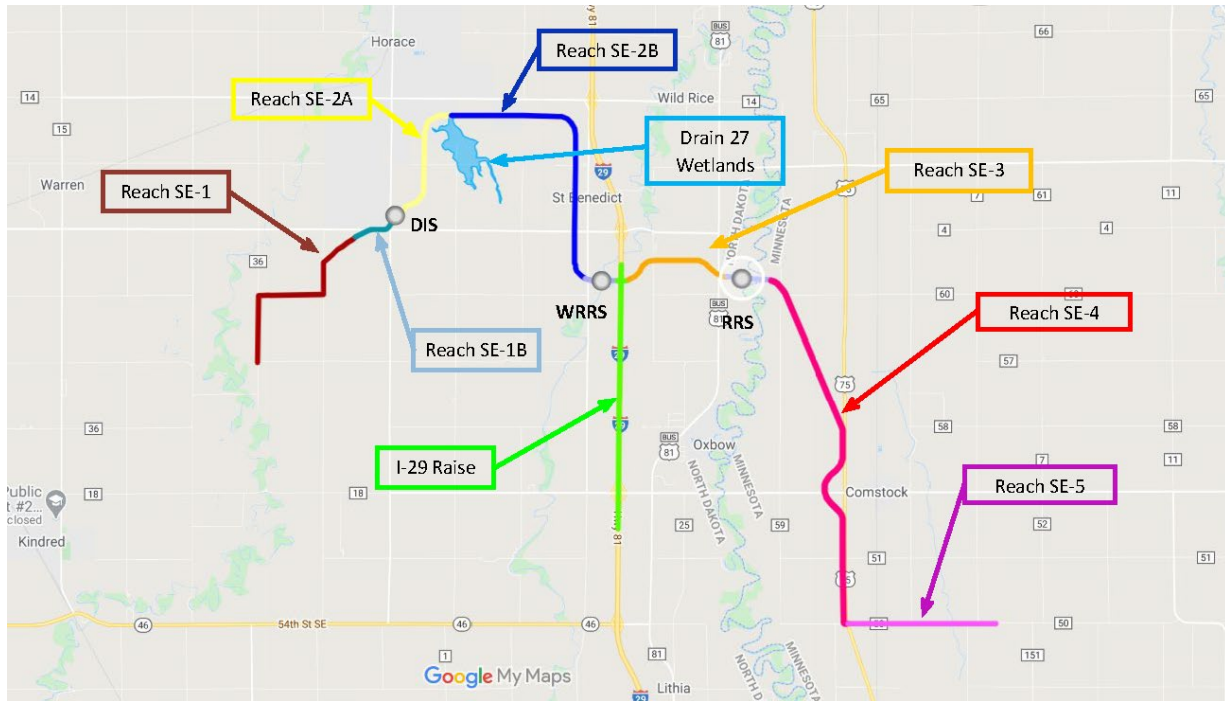

***Fargo-Moorhead Metro FRM – Federal Work/Southern Embankment and Control Structures***

DIS = Diversion Inlet Control Structure

WRRS = Wild Rice River Control Structure

RRS = Red River Control Structure
