



# FARGO MOORHEAD DIVERSION PROJECT

# MONTHLY UPDATE

14 May 2025

## 1 Diversion Inlet Structure (DIS) – Construction

Structure includes 3-50 ft. wide Tainter gates. Construction is 99% complete. Completion date is 30 June 25. Operating machinery corrections complete. Final inspections and training upcoming. Turnover to Sponsors for OMRRR anticipated in July 2025.

## 2 Wild Rice River Structure (WRRS) – Construction

Structure includes 2-40 ft. wide Tainter gates. Construction is 98% complete. Completion date is 6 August 2025. Operating machinery corrections, final inspections and training upcoming. Turnover to Sponsors for OMRRR anticipated in September 2025.

## 3 Red River Structure (RRS) - Construction

Structure includes 3-50 ft. wide Tainter gates. Construction is 74% complete. Construction completion date is 29 April 2026. East and west dam wall and approach apron construction continues. Gate machinery is on site and will be installed once mechanical platform bridge complete.

## 4 Southern Embankment – Reach SE-2A - Construction

Construction is 76% complete but continues to be behind schedule. Scheduled completion date of 13 October 2024 was not met. Revised schedule and completion date pending.

## 5 Drain 27 Wetland Mitigation Project Plantings - Construction

Native plantings 5-year contract for wetland establishment. Completion date is 1 December 2027. Contractor replanting areas disturbed by adjacent producers.

## 6 FY2024 Contract Awards - Construction:

OHB Ring Levee: 50% complete. Contractor digging inspection trench. Contract completion date is 24 September 2025.

Reach SE-1B: 31% complete. CR16/17 intersection closed to allow completion of road work and tie in of embankment to the Diversion Inlet Structure. Contract completion date is 13 March 2026.

Reach SE-2B: 45% complete. Contractor preparing to place embankment. Contract completion date is 23 August 2026.

Forest Mitigation #1: Contractor is planting. Contract completion date is 31 Dec 2028.

Reach SE-4: 5% complete. Contractor is performing earthwork activities. Contract completion date is 3 June 2026.

## 7 FY2025 Contract Awards - Construction:

SE-3: Contractor stripping topsoil. Contract completion date is 11 September 2026.

SE-5: Contractor is mobilizing and stripping topsoil. Contract completion date is 8 August 2026.


Forest Mitigation #2: Contractor is planting. Contract completion date is 31 Dec 2029.

## 8 I-29 Raise – Operations and Maintenance (OMRRR)

Turnover to MFDA occurred on 20 December and preparation of O&M documents is ongoing.

## 9 Drayton Dam Mitigation Project Design - Operations and Maintenance (OMRRR)

Turnover to MFDA for O&M occurred on 28 Nov 2023. OMRRR manual coordination continues.

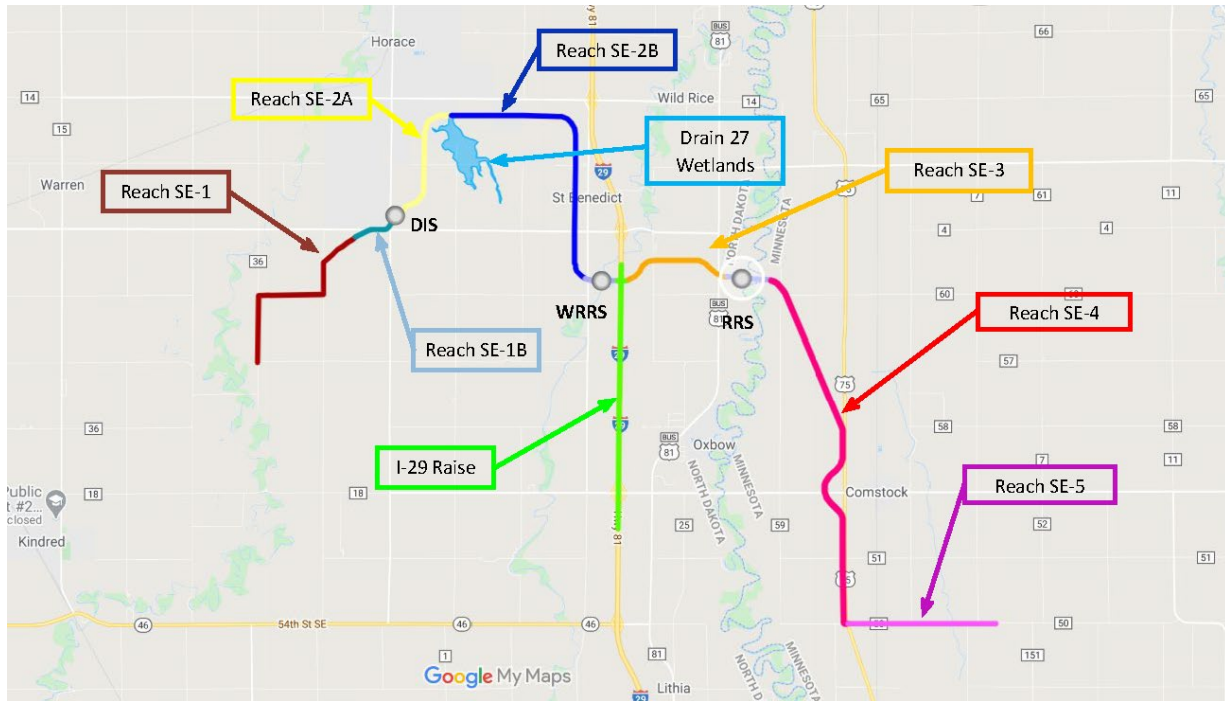

***Fargo-Moorhead Metro FRM – Federal Work/Southern Embankment and Control Structures***

DIS = Diversion Inlet Control Structure

WRRS = Wild Rice River Control Structure

RRS = Red River Control Structure
