



FARGO MOORHEAD DIVERSION PROJECT

MONTHLY UPDATE

24 July 2025

1 Diversion Inlet Structure (DIS) – Construction

Structure includes 3-50 ft. wide Tainter gates. Construction is 99% complete. Completion date is now 28 Oct 2025. Training held 19 June. Final inspections upcoming. Turnover to Sponsors for OMRRR anticipated in November 2025.

2 Wild Rice River Structure (WRRS) – Construction

Structure includes 2-40 ft. wide Tainter gates. Construction is 98% complete. Completion date is now 28 November 2025. Operating machinery corrections, final inspections and training upcoming. Turnover to Sponsors for OMRRR anticipated in December 2025.

3 Red River Structure (RRS) - Construction

Structure includes 3-50 ft. wide Tainter gates. Construction is 81% complete. Construction completion date is 30 April 2026. East and west dam wall and approach apron and gate machinery install ongoing. Red River re-route rescheduled for 7 Aug 2025 due to wet and high river conditions.

4 Southern Embankment – Reach SE-2A - Construction

Construction is 76% complete but continues to be behind schedule. Scheduled completion date of 13 October 2024 was not met. Revised schedule and completion date pending.

5 Drain 27 Wetland Mitigation Project Plantings - Construction

Native plantings 5-year contract for wetland establishment. Completion date is 1 December 2027. Contractor replanting areas disturbed by adjacent producers.

6 FY2024 Contract Awards - Construction:

OHB Ring Levee: 50% complete. Levee construction ongoing. Contractor digging inspection trench. Contract completion date is 17 October 2025.

Reach SE-1B: 36% complete. Anticipate opening CR16/17 by October 2025. Contract completion date is 13 March 2026.

Reach SE-2B: 45% complete. Embankment construction ongoing. Paving of CR16 crossing pending. Contract completion date is 23 August 2026.

Forest Mitigation #1: Contractor is planting. Contract completion date is 31 Dec 2028.

Reach SE-4: 9% complete. Embankment construction continues. road work. Contract completion date is 30 September 2026.

7 FY2025 Contract Awards - Construction:

SE-3: 2% complete. Embankment construction continues. Contract completion date is 11 September 2026.

SE-5: Contractor is clearing and grubbing. Wolverton Creek crossing must be complete by 15 Nov 2025. Contract completion date is 8 September 2026.


Forest Mitigation #2: Contractor is planting. Contract completion date is 31 Dec 2029.

8 I-29 Raise – Operations and Maintenance (OMRRR)

Turnover to MFDA occurred on 20 December and preparation of O&M documents is ongoing.

9 Drayton Dam Mitigation Project Design - Operations and Maintenance (OMRRR)

Turnover to MFDA for O&M occurred on 28 Nov 2023. OMRRR manual coordination continues.

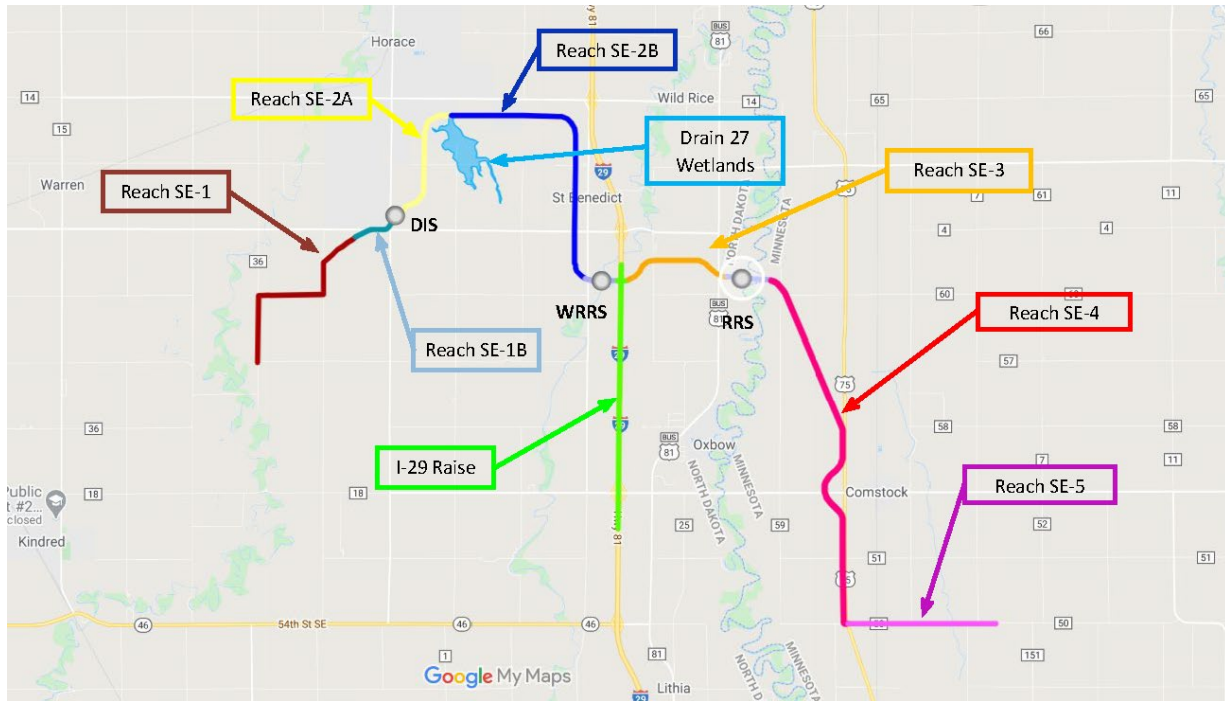

Fargo-Moorhead Metro FRM – Federal Work/Southern Embankment and Control Structures

DIS = Diversion Inlet Control Structure

WRRS = Wild Rice River Control Structure

RRS = Red River Control Structure
