

# Flood Diversion Authority January Report

Presented by

Program Management Consultant

January 14, 2016

# In Town Levees

## WP-42A.1/A.3 (4th St N Pump Station) – January 2016



Continuing work on electrical inside pump station.

# In Town Levees

## WP-42A.1/A.3 (4th St N Pump Station) – January 2016



Continuing work on Outfall box culvert.

# In Town Levees

## WP-42A.1/A.3 (4th St N Pump Station) – January 2016



# In Town Levees


## WP-C.2 (Park East Demolition) – January 2016

Demolition of apartment buildings started.



# In Town Levees

## WP-42A.2 (2<sup>nd</sup> Street Pump Station) – January 2016

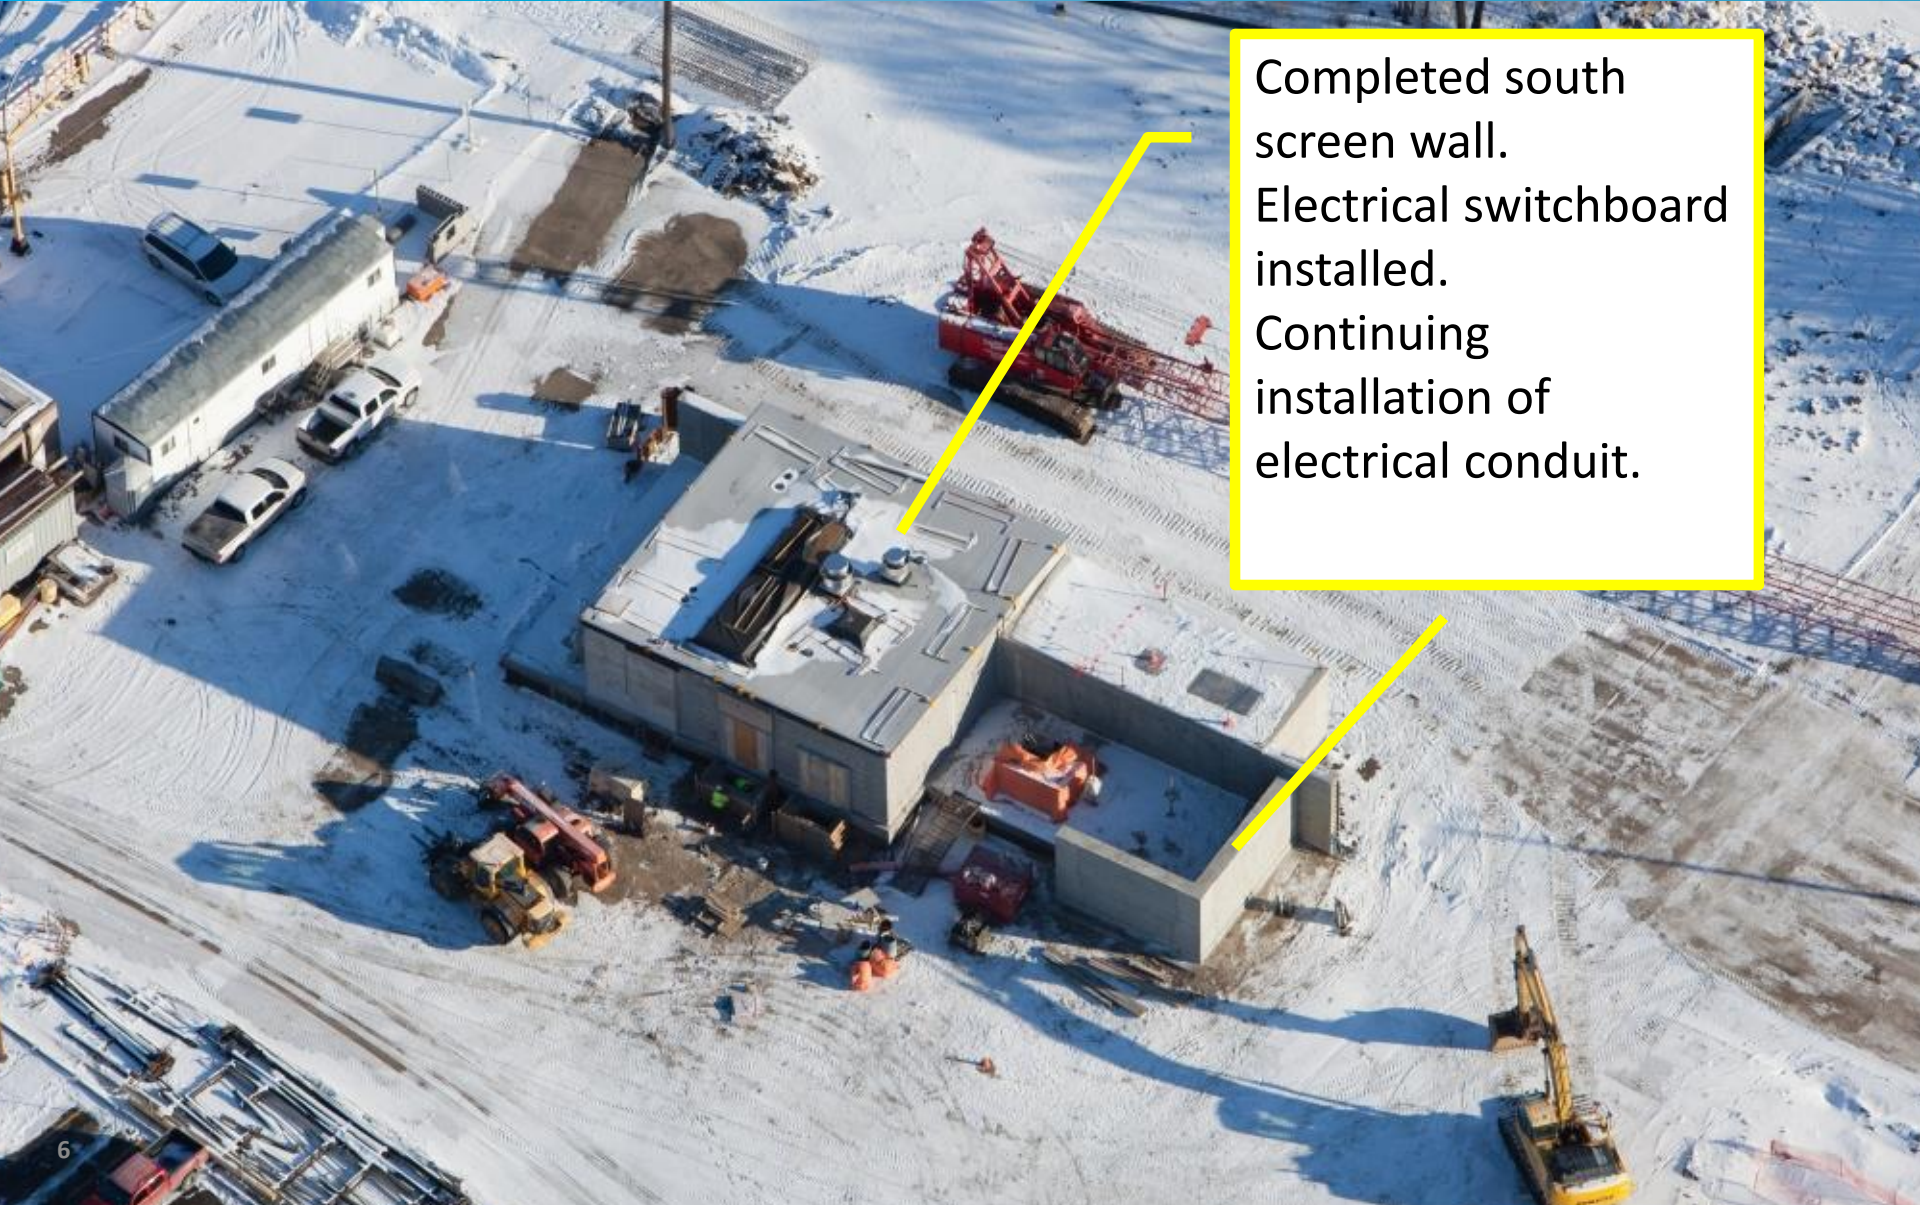

Completed south screen wall.  
Electrical switchboard installed.  
Continuing installation of electrical conduit.

# In Town Levees WP-42A.2 (2<sup>nd</sup> Street Pump Station)




# In Town Levees WP-42A.2 (2<sup>nd</sup> Street Pump Station)





# In Town Levees

## WP-42F.1S (2<sup>nd</sup> Street Flood Control) – January 2016

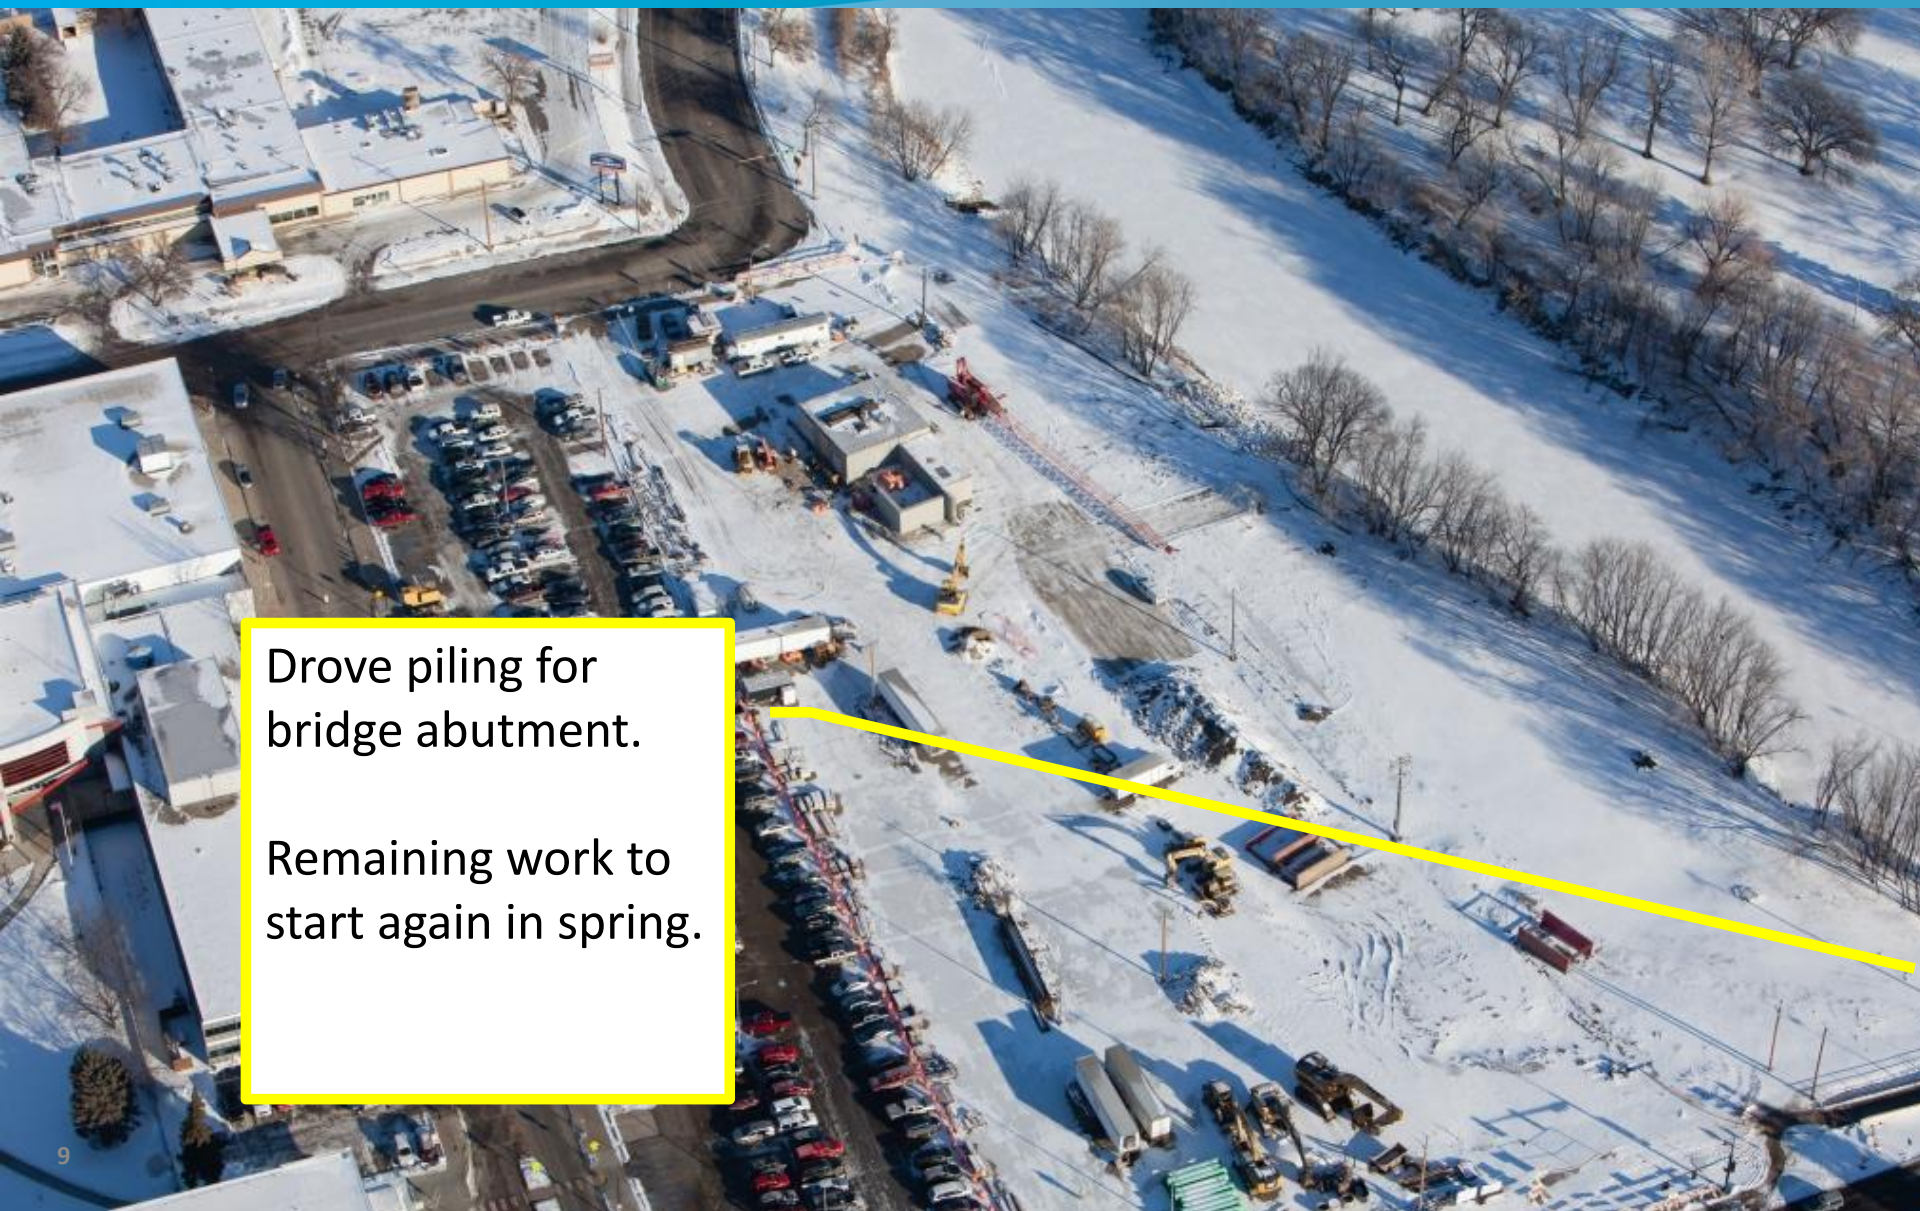

Drove piling for  
bridge abutment.

Remaining work to  
start again in spring.

# WP-43 (OHB Golf Course and Development) – January 2016

18 homes under  
construction and 7 closed.



# WP-43E.2B (Oxbow Home Move) – January 2016

Preparing home  
for move.



# January/February Priority Areas

## 💧 WP-42: In Town Levees

– *Construction, demolition, and land acquisition*

## 💧 WP-43: OHB

– *Acquisitions, relocations, home move (1), and home construction*

## 💧 MN DEIS - developing responses to comments

## 💧 Permit Preparation - 404, Dam Safety

## 💧 Public Private Partnership (PPP) - Development of procurement documents

## 💧 Negotiation of PPA with Corps

## 💧 Schedule and Cost Estimate – 2015 update

# Planned Bid Schedule – In Town Levees

- 💧 WP-42C.1 (Demolition) – Jan 21, 2016
  - *Howard Johnson's, Shakey's, Fargo Public Schools*
- 💧 WP-42H.2 (El Zagal Phase 2 Levee) – Jan 26 2016
  - *Demolition, Levee, roadway closure*
- 💧 WP-42I.1 (Mickelson Levee Extension) – Feb 9, 2016
  - *Demolition, Levee*
- 💧 WP-42F.1N (Flood Control 2nd St N) – Mar 2016
  - *Floodwall, road relocation*
- 💧 WP-42F.2 (Flood Control 2nd St. South) – April 2016
  - *Levee, roadway closure*

# Next

💧 Corps of Engineers report
