

Flood Diversion Authority October Report

Presented by

Program Management Consultant

October 8, 2015

Planned Bid Schedule – In Town Levees

- 💧 WP-42C.1 (Demolition) – Jan 2016
 - *Howard Johnson's, Shakey's, Fargo Public Schools*
- 💧 WP-42H.2 (El Zagal Phase 2 Levee) – Jan 2016
 - *Demolition, Levee, roadway closure*
- 💧 WP-42I.1 (Mickelson Levee Extension) – Feb 2016
 - *Demolition, Levee*
- 💧 WP-42F.1N (Flood Control 2nd St N) – Mar 2016
 - *Floodwall, road relocation*
- 💧 WP-42F.2 (Flood Control 2nd St. South) – Mar 2016
 - *Levee, roadway closure*

In Town Levees

WP-42A.1/A.3 (4th St N Pump Station) – October 2015




Completed at grade slab for the pump station

In Town Levees

WP-42A.1/A.3 (4th St N Pump Station) – October 2015

Continuing work on
outfall box culvert
base slabs, walls and
lids

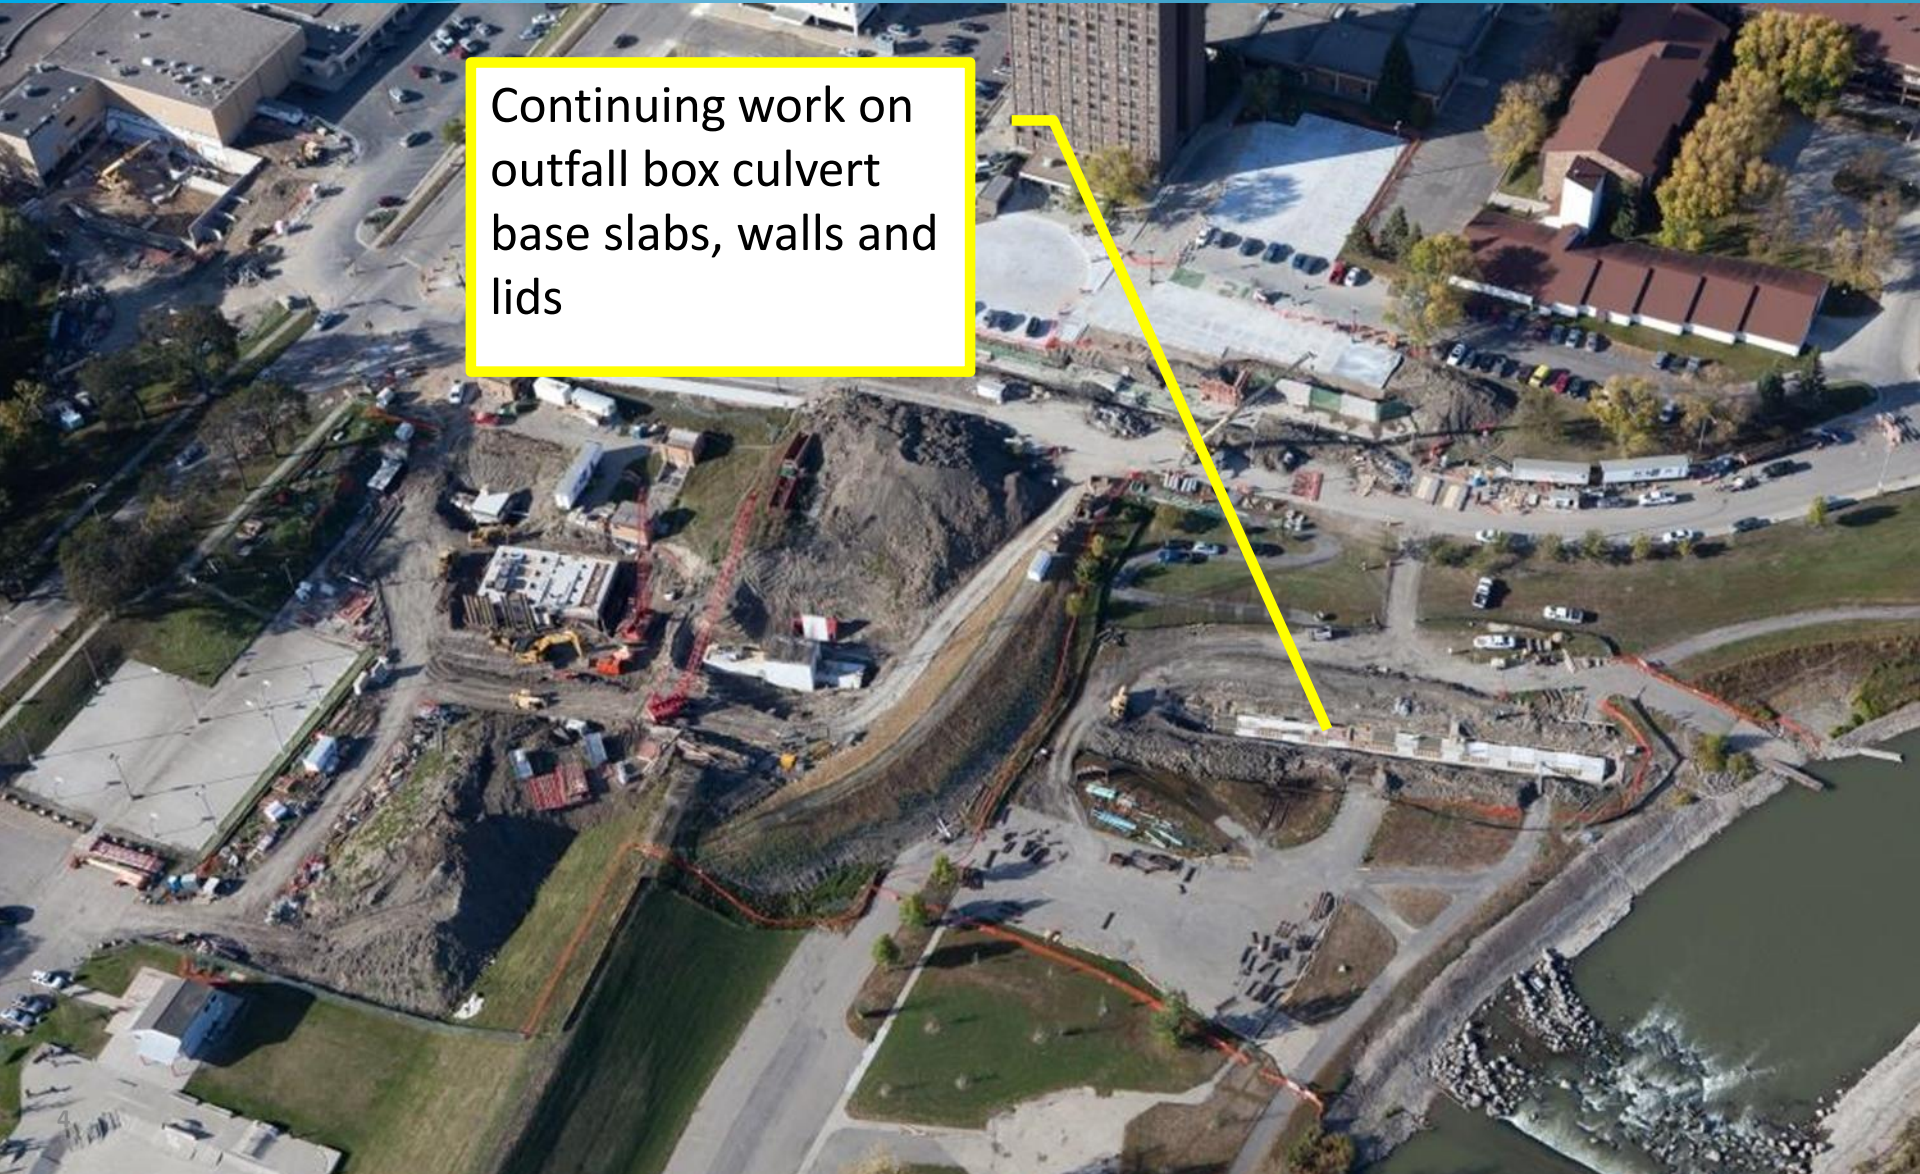

In Town Levees

WP-42A.1/A.3 (4th St N Pump Station) – October 2015

Continuing work on the floodwall footings and wall sections



In Town Levees

WP-42A.1/A.3 (4th St N Pump Station) – October 2015

High rise parking lot east nearly complete



In Town Levees WP-42A.2 (2nd St N Pump Station) – October 2015



Started above
ground masonry
walls

In Town Levees WP-42A.2 (2nd St N Pump Station) – October 2015



Installing pump station discharge pipe

In Town Levees - WP-42F.1S (Flood Control, 2nd St N, South of Pump Station) – October 2015



Started clearing and grubbing


In Town Levees - WP-42F.1S (Flood Control, 2nd St N, South of Pump Station) – October 2015



Installed
construction fencing

In Town Levees

WP-42H.2 (El Zagal Phase 1) – October 2015

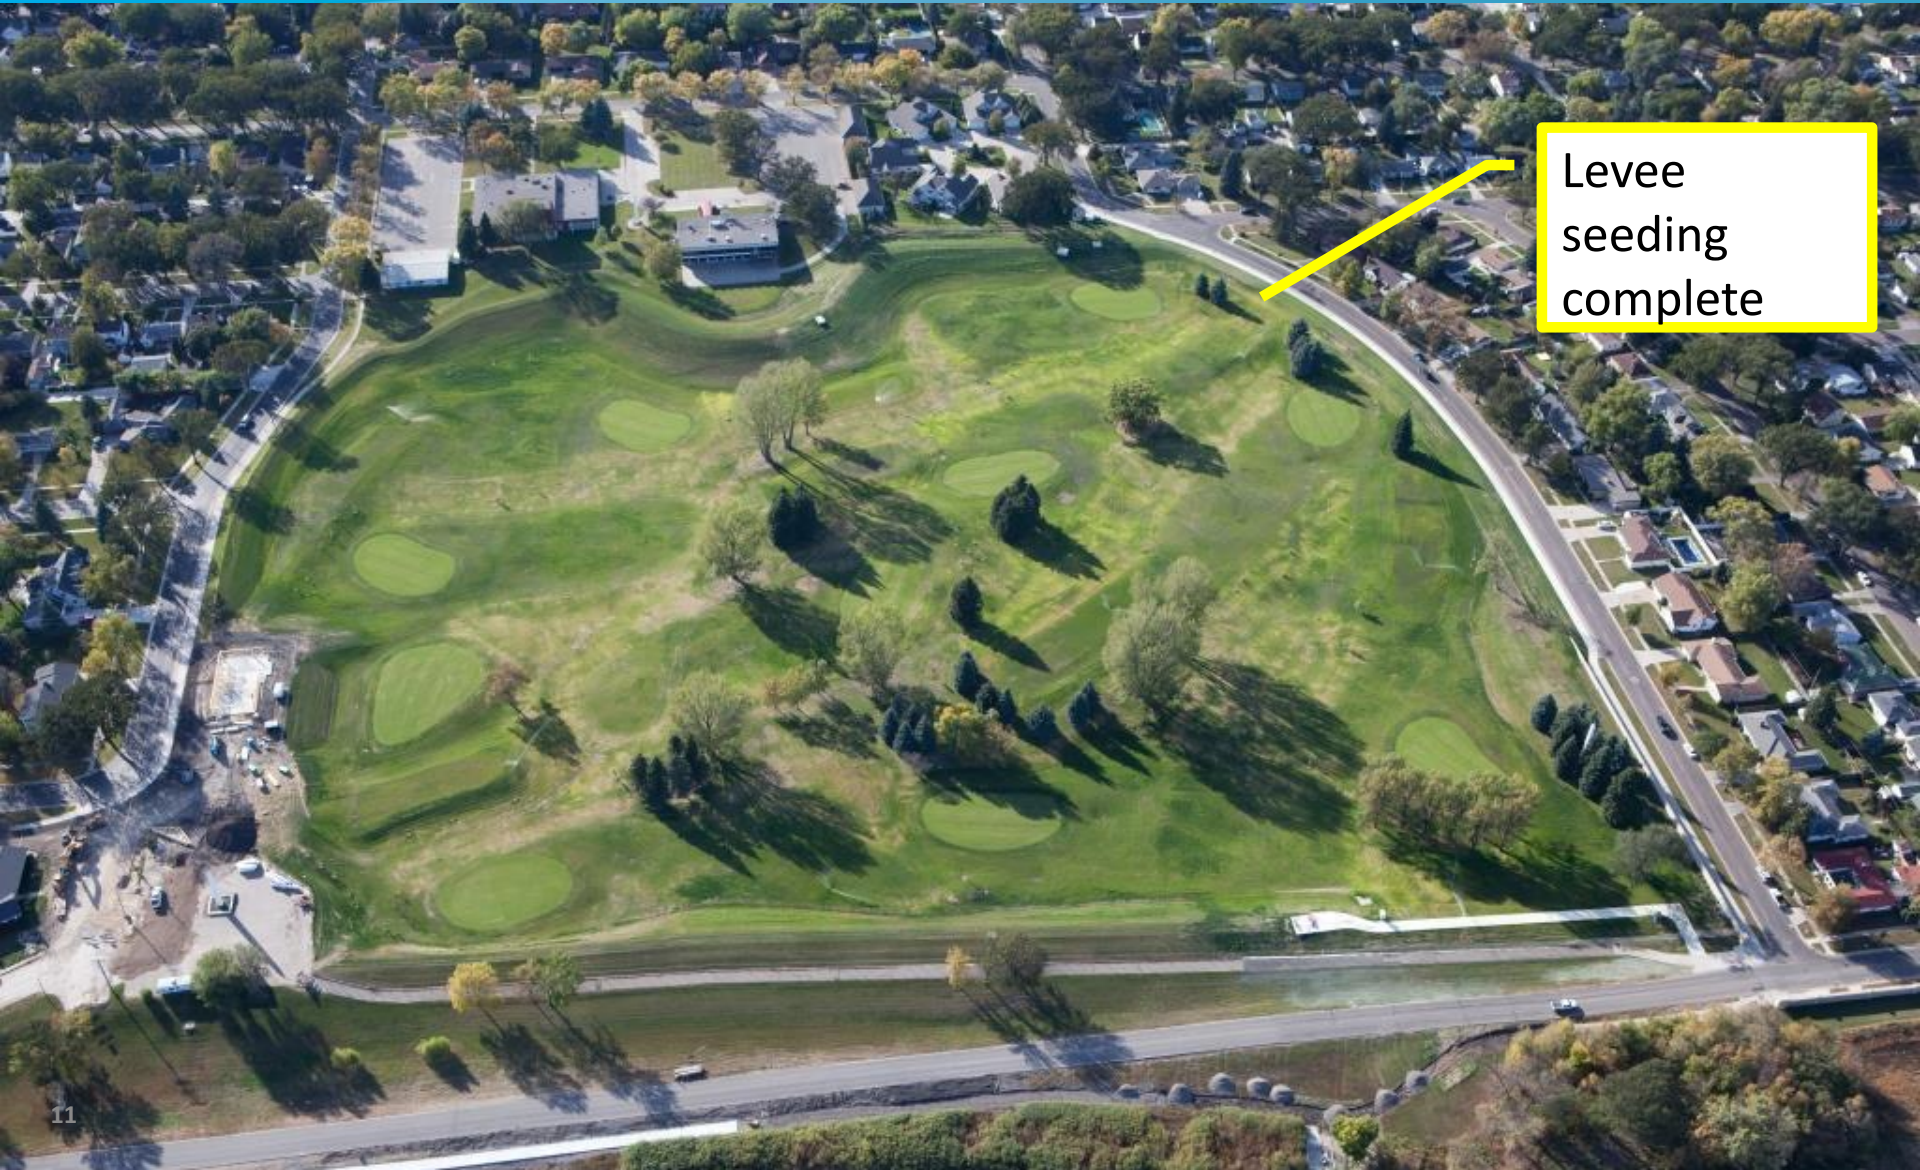

Levee
seeding
complete

WP-43 (OHB Golf Course and Development) – October 2015

18 houses under
construction or have
closed



WP-43 (Oxbow Replacement Home Construction) – October 2015



6 homes are complete and owners have been relocated

WP-43 (Oxbow Golf Course Construction) – October 2015



Continuing work on
Club house foundation
and walls

October/November Priority Areas

💧 WP-42: In Town Levees

- *Construction, cultural mitigation and land acquisition*

💧 WP-43: OHB

- *Acquisitions, relocations, demolitions/moves (2), and home construction*

💧 Permit Preparation and Coordination with USACE

💧 Public Private Partnership (PPP)

- *Development of procurement documents*

💧 Schedule and Cost Estimate – 2015 update

Requests for Qualifications/Quotations

💧 Landscaping Architect (CCJWRD)

MN Draft EIS

💧 Public Meeting

- *Courtyard Marriott in Moorhead, MN - Oct 14, 2015*
- *Open House from 5:00 – 10:00 PM*
- *Welcome and Brief Presentation at 7:00 PM*
- *Public Comments from 7:30 – 10:00 PM*

💧 Comment Period Ends – Oct 28, 2015
